ID		Task Mode	Task Name	Duration	Start	Finish
1			**1 unit 14,000L Helicopter Bowser**	**221 days**	**Fri 29-01-21**	**Tue 16-11-21**
2			PO Received	1 day	Fri 29-01-21	Fri 29-01-21
3			Deposit received	3 days	Sat 30-01-21	Wed 03-02-21
4			**Engineering**	**14 days**	**Wed 03-02-21**	**Tue 23-02-21**
5			Drawings preparation	14 days	Wed 03-02-21	Tue 23-02-21
6			**Procurement**	**120 days**	**Tue 23-02-21**	**Thu 29-07-21**
7			**Refueler Module from Proflo Ind. (inclusive shipment to M'sia)**	120 days	Tue 23-02-21	Thu 29-07-21
8			**Aluminum Tank Barrel (inclusive shipment to M'sia)**	65 days	Tue 23-02-21	Wed 19-05-21
9			HINO FL8J 6x2 Truck Chassis	2 days	Tue 01-06-21	Wed 02-06-21
10			PTO	14 days	Tue 01-06-21	Fri 18-06-21
11			Tank fittings & manhole covers etc	14 days	Tue 01-06-21	Fri 18-06-21
12			**Fabrication & Assembly of Bowser**	**105 days**	**Thu 03-06-21**	**Mon 18-10-21**
13			Chassis modification works	4 days	Thu 03-06-21	Wed 09-06-21
14			Tank mounting	5 days	Wed 09-06-21	Tue 15-06-21
15			Refueler module mounting	7 days	Fri 30-07-21	Sat 07-08-21
16			Hydraulic system installation	7 days	Sat 07-08-21	Wed 18-08-21
17			Pneumatic system installation	7 days	Wed 18-08-21	Thu 26-08-21
18			Electrical wiring installation	7 days	Thu 26-08-21	Mon 06-09-21
19			Final hook up of refueler system (sensors, PLC, etc.) with Proflo Technician	14 days	Mon 06-09-21	Thu 23-09-21
20			Final testing & troubleshooting	5 days	Fri 24-09-21	Thu 30-09-21
21			Painting works	5 days	Thu 30-09-21	Wed 06-10-21
22			**Factory Acceptance Test (with client)**	2 days	Wed 06-10-21	Fri 08-10-21
23			Re-work (if any)	5 days	Fri 08-10-21	Fri 15-10-21
24			Pre-Delivery inspection (by client)	2 days	Fri 15-10-21	Mon 18-10-21
25			**Ready for delivery (Ex-factory IGZE)**	1 day	Mon 18-10-21	Wed 20-10-21
26			**Sea shipment to Sabah**	16 days	Wed 20-10-21	Wed 10-11-21
27			**Training & Commissioning at KK Navy base**	5 days	Wed 10-11-21	Tue 16-11-21

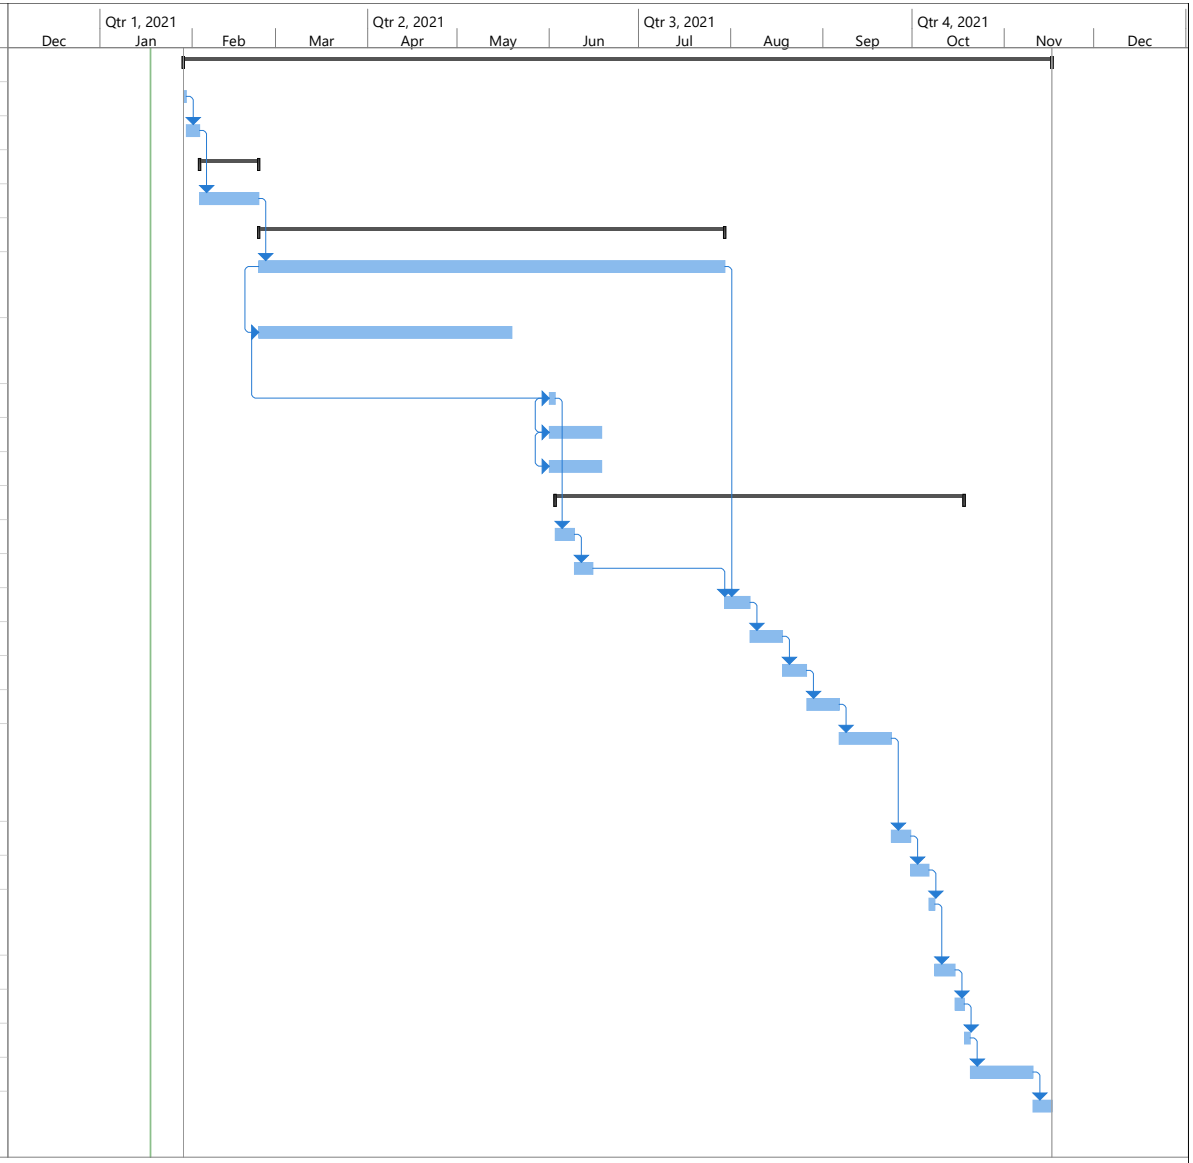

Project: 1 unit 14kL Bowser Pro
Date: Mon 18-01-21

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
